




US Army Corps
of Engineers ®

P2 - RMS Interface

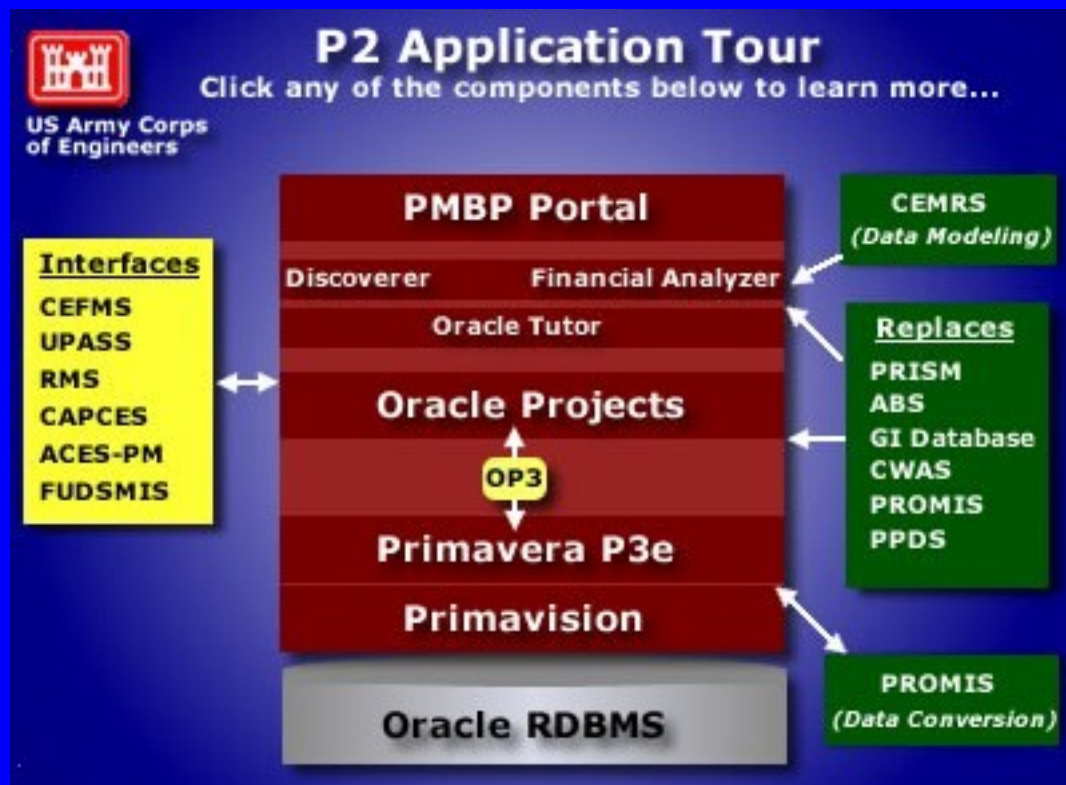


May 2010



US Army Corps
of Engineers ®

P2 - RMS Interface

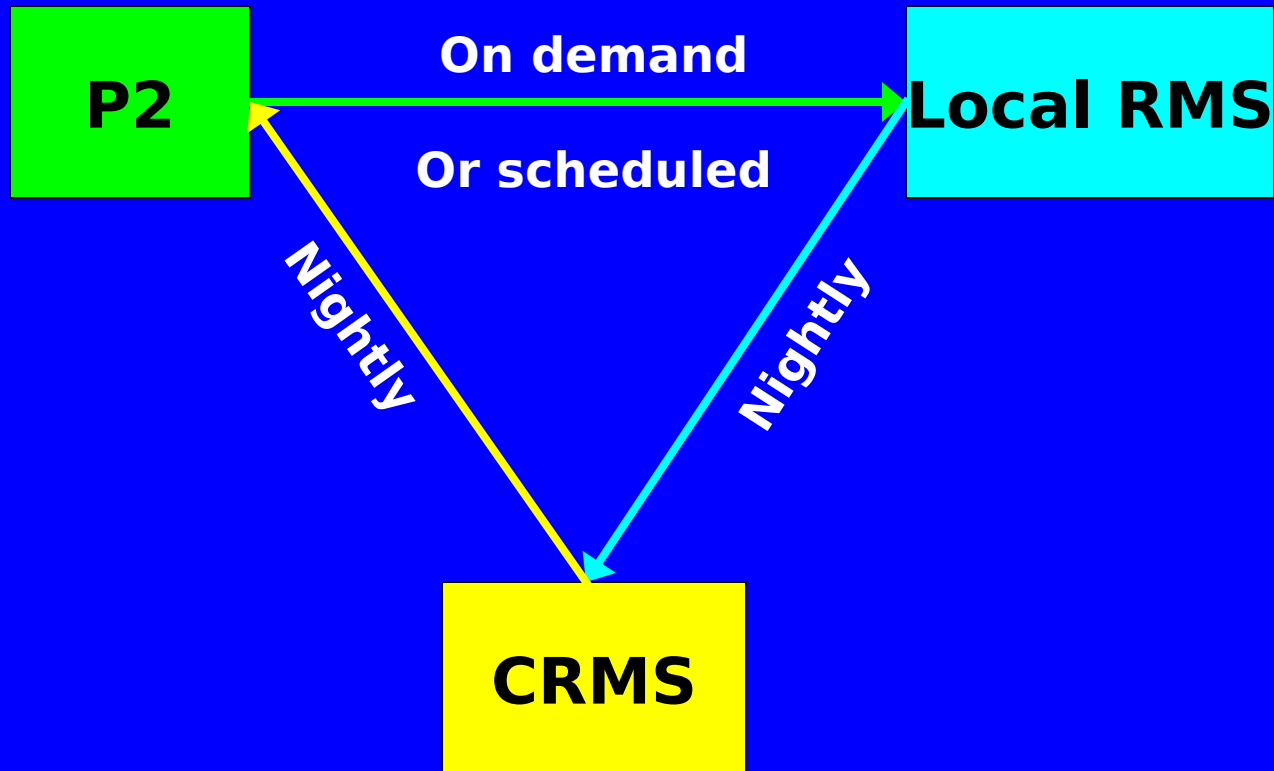



US Army Corps
of Engineers ®

P2 - RMS Interface

- One P2 Project to one RMS Contract
- One P2 Project to multiple RMS Contracts
- Multiple P2 Projects to one RMS Contract



US Army Corps
of Engineers ®

P2 - RMS Interface

- Schedule Dates
 - P2 controls prior to Contract Award
 - RMS controls after Contract Award
- P2 controls budget
- CEFMS controls funds



US Army Corps
of Engineers

RMS download from P2

- **Project Information**

- **Project ID**
- **Project Title**
- **WBS**
- **WBS Title**
- **Task Code**
- **Task Name**
- **Task Amount**
- **Design By**
- **Contract Type**
- **Project - Scope of Work**
- **Contract Status Code**
- **Primary Delay Code**
- **Project - Customer Issues**
- **Project - USACE Issues**
- **Task Organization (P2 Org Code)**

- **Milestone Dates (Target Dates)**


- **Contract Award Date**
- **NTP Acknowledged Date**
- **Contract Required Completion Date**
- **Construction Completion Date**
- **Beneficial Occupancy Date**
- **Physical Completion Date**
- **Transfer Document Date**
- **AE Evaluation Date**
- **Contractor Evaluation Date**
- **Contractor Final Payment Date**



US Army Corps
of Engineers

CRMS download to P2

- **Contract Information**
 - **Contract Number**
 - **Delivery Order Number**
 - **Contract Title**
 - **Contract Scope of Work**
 - **Contract Amount**
 - **Placement Percentage**
 - **Contract Status Code**
 - **Primary Delay Code**
 - **Phase (WBS) Title**
 - **Contract - Customer Issues**
 - **Contract - USACE Issues**
 - **Phase Title on Multiphase Contracts**
- **Milestone Dates**
 - **Contract Award Date**
 - **NTP Acknowledged Date**
 - **Contract Required Completion Date**
 - **Construction Completion Date**
 - **Beneficial Occupancy Date**
 - **Physical Completion Date**
 - **Transfer Document Date**
 - **AE Evaluation Date**
 - **Contractor Evaluation Date**
 - **Contractor Final Payment Date**

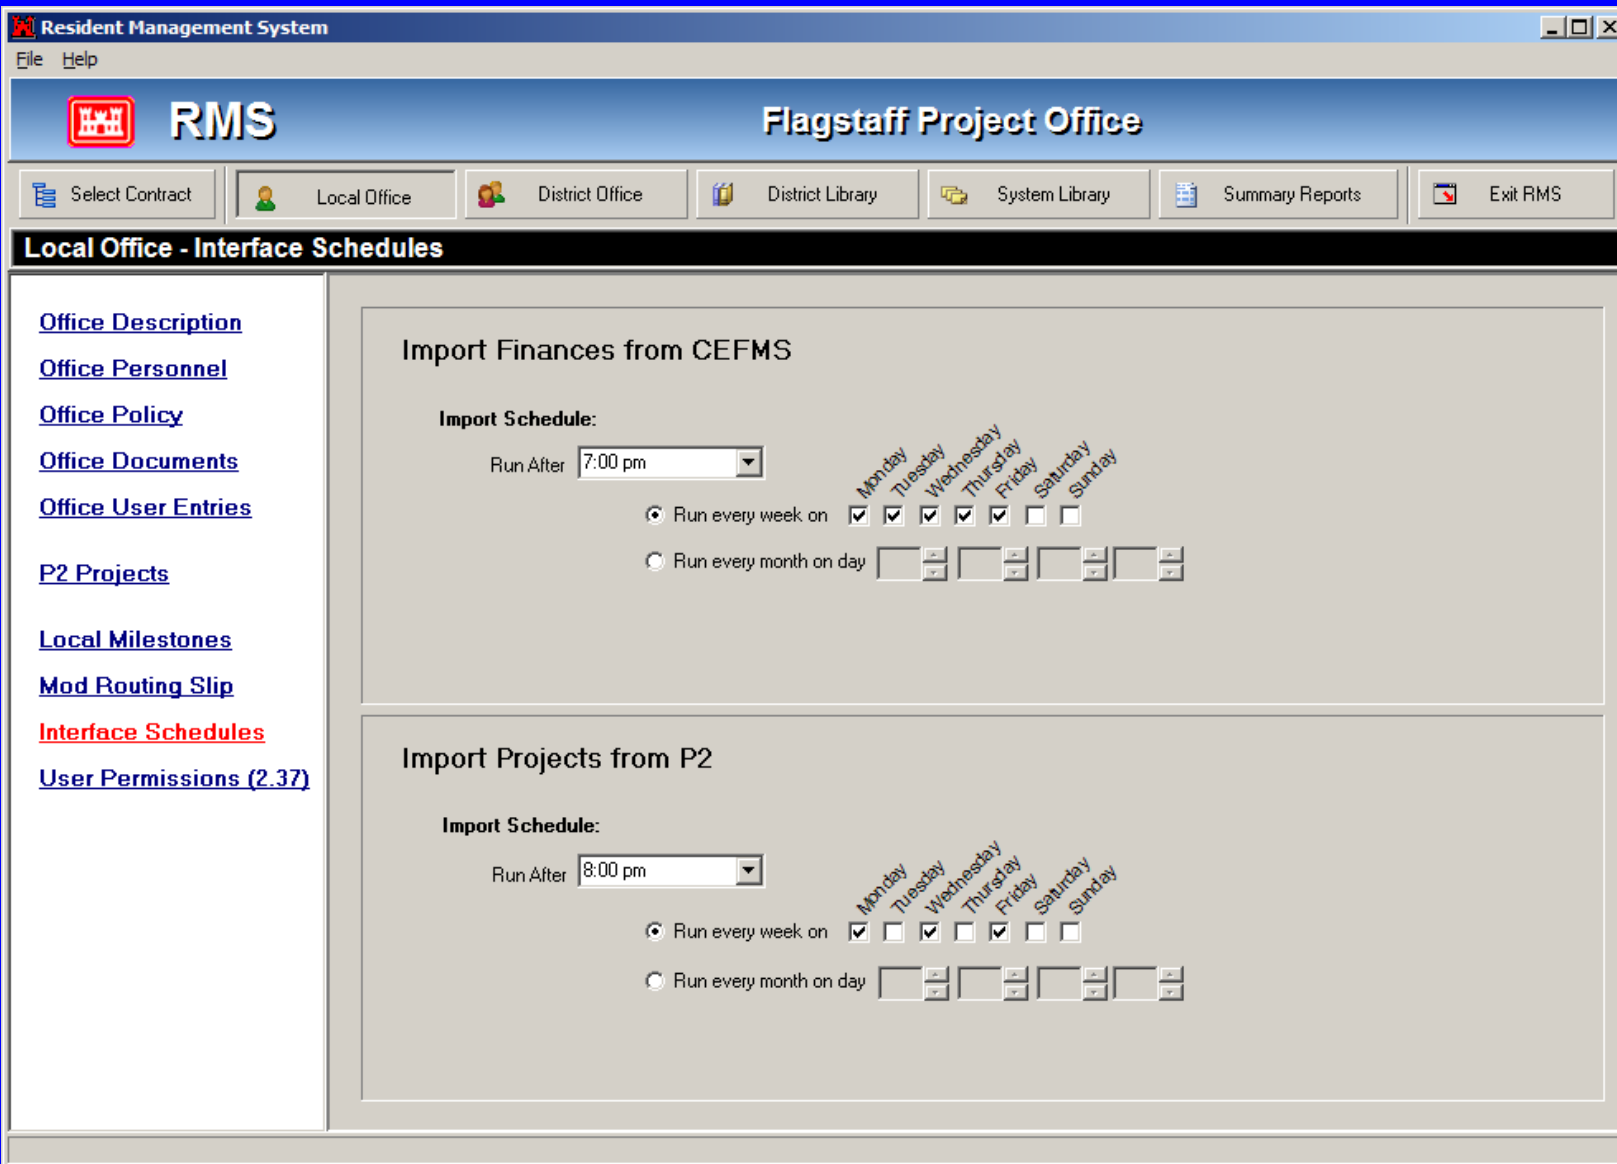

P2 Project ID and Project Title

WBS No. and WBS Title

Task Code / Activity ID

Primavera Enterprise - Project Manager: 104777 (Port of Los Angeles)

File Edit View Project Enterprise Tools Admin Help

Activities

Layout: Classic Schedule Layout Filter: Activities

Activity Name	Activity ID	Milestone - Civil Works	Milestone - Construct...	RMS Interface
104777.30000.30D00 Construction Contract				
104777.30000.30D00.30D50 Dredge Construction Contract (188.9 mil/144.8 mil Expanded)				
Contract Ready to Advertise (RTA)	CON1920	Cw400		
Contract Advertised	CON2180	Cw420		
Open Bids	CON2220	Cw430		
Award Contract	CON2260		CC800	RMS_M_CONTRACT_AW
CC-Notice to Proceed	CON2280	Cw440		
Construction NTP Acknowledgement	CON2281		CC810	RMS_NTP_ACKNOWLEDG
SW SLIP Area (1) Preparation for Surcharge (Area 2 + Mini...	CON2379			
D203 Pit 1 Mining	CON23791			
Mining Material Disposal (P300)	CON23792			
Mining Material Disposal (CSWH)	CON23793			
Mining Material Disposal (Surcharge Area 1)	CON23794			
Backfilling Mining Pit 1 (From D204/207/210)	CON23795			
Added Disposal Area Preparation (Expansion P300)	CON23796			
Dredging of Main Channel (D210/207)	CON23797			
Added/Berth Dredging/Wharf Construction	CON23798			
Construction Contract L1000319 - NED GNF, Federal Fun...	CON23800			RMS_A_CONTRACT
Construction Contract L1000319 - O&M, Federal Funding	CON23801			RMS_A_CONTRACT
Construction Contract L1000319 - NED GNF, Non Federal...	CON23802			RMS_A_CONTRACT
Construction Contract L1000319 - LERR - Non Federal Fu...	CON23803			RMS_A_CONTRACT
Construction Contract L1000319 - Incremental - Non Feder...	CON23804			RMS_A_CONTRACT
Construction Contract L1000319 - Local Service Facilities ...	CON23805			RMS_A_CONTRACT
Construction Contract L1000319 - Betterments - Non Fede...	CON23806			RMS_A_CONTRACT
Construction Contract L1000319 - Advance Funds	CON23807			RMS_A_CONTRACT
Supervision & Administration - Federal Funding	CON23808			
Supervision & Administration - Non Federal Funding	CON23809			

October 2004
03 10 17

Add
Delete

Information that is interfaced between RMS and P2.

Construction Milestones

P2 construction tasks linked to an RMS Contract

General Status Resources Predecessors Successors Codes

Portfolio: SPD Projects User: lled9rl Data Date: 03-Apr-01 Access Mode: Shared Baseline: Current Project

Start | Inbox ... | DA722... | Micros... | M:\W\I... | 03:11



US Army Corps
of Engineers

P2 Project Number and Title

WBS/Activity Costs

Milestone Dates

Primavera Enterprise - Project Manager: 108791 (B2 523 SELA Orl Par, LA, UF)

Activities

Layout: VPM Classic WBS Layout Filter: All Activities

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Budgeted Total Cost	Actual Total Cost	Remaining Total Cost	At Completion Total Cost	Resource IDs
100791.300001.30050	DACW29-99-C 0016NA SELA Broad St PS#1	1636.0d	17-Dec-99 A	20-Apr-05	1422.0d	\$404,623.75	\$0.00	\$404,624.19	\$404,624.19	
M14500	Contract Nego/Rec Docs	0.0d	02-Aug-04	02-Aug-04	1602.0d	\$0.00	\$0.00	\$0.00	\$0.00	
M14600	Contract RTA	0.0d	02-Aug-04	02-Aug-04	1602.0d	\$0.00	\$0.00	\$0.00	\$0.00	
M14700	Receive Sponsor Construction Funds	0.0d	02-Aug-04	02-Aug-04	1602.0d	\$0.00	\$0.00	\$0.00	\$0.00	
M14800	CRD Announcement	0.0d	02-Aug-04	02-Aug-04	1602.0d	\$0.00	\$0.00	\$0.00	\$0.00	
M14900	Contract Adv/RFP Issued	0.0d	02-Aug-04	02-Aug-04	1602.0d	\$0.00	\$0.00	\$0.00	\$0.00	
M15000	Draws Bacon Wage Rates	0.0d	02-Aug-04	02-Aug-04	1602.0d	\$0.00	\$0.00	\$0.00	\$0.00	
M15100	Gov't Estimate (IGE)	0.0d	02-Aug-04	02-Aug-04	1602.0d	\$0.00	\$0.00	\$0.00	\$0.00	
M15200	Open Bids	0.0d	02-Aug-04	02-Aug-04	1602.0d	\$0.00	\$0.00	\$0.00	\$0.00	
M15300	Abs of Bids/Rec of Nego	0.0d	02-Aug-04	02-Aug-04	1602.0d	\$0.00	\$0.00	\$0.00	\$0.00	
M15400	Cert Low Bid/Prep Contract Docs	0.0d	02-Aug-04	02-Aug-04	1602.0d	\$0.00	\$0.00	\$0.00	\$0.00	
M15500	Rec Bonds/Prep NTP	0.0d	02-Aug-04	02-Aug-04	1602.0d	\$0.00	\$0.00	\$0.00	\$0.00	
M15600	Evaluate A/E Contractor	0.0d	02-Aug-04	02-Aug-04	1602.0d	\$0.00	\$0.00	\$0.00	\$0.00	
M15700	Eval Const Contractor	0.0d	02-Aug-04	02-Aug-04	1602.0d	\$0.00	\$0.00	\$0.00	\$0.00	
M15800	All Other Awd Docs	0.0d	02-Aug-04	02-Aug-04	1602.0d	\$0.00	\$0.00	\$0.00	\$0.00	
M15900	Budgeted Construction Contingency	0.0d	02-Aug-04	02-Aug-04	1602.0d	\$0.00	\$0.00	\$0.00	\$0.00	
M17000	0-10 Construction NTP Acknowledged	0.0d	22-Dec-99 A			\$0.00	\$0.00	\$0.00	\$0.00	
M18000	0-10 Contract 99C0016	25.0d	22-Dec-99 A	03-Feb-04 A	1405.0d	\$404,623.75	\$0.00	\$404,624.19	\$404,624.19	CONSTSVCS, B2P0400-CONTRACTING
M18100	0-10 Physical Completion	0.0d		21-Aug-02 A		\$0.00	\$0.00	\$0.00	\$0.00	
M18200	0-10 Contract Fiscal Completion	0.0d		20-Apr-05	1422.0d	\$0.00	\$0.00	\$0.00	\$0.00	
M18300	0-10 Contract Award	0.0d		17-Dec-99 A		\$0.00	\$0.00	\$0.00	\$0.00	
M18400	0-10 Construction Completion	0.0d		03-Feb-04 A		\$0.00	\$0.00	\$0.00	\$0.00	
M18500	0-10 Contract Transfer Document Date	0.0d		20-Apr-05	1422.0d	\$0.00	\$0.00	\$0.00	\$0.00	
M18600	0-10 Contract Required Completion	0.0d		03-Mar-02*	1495.0d	\$0.00	\$0.00	\$0.00	\$0.00	
M18700	0-10 AE Evaluation Date	0.0d		02-Aug-04	1602.0d	\$0.00	\$0.00	\$0.00	\$0.00	

General Status Resources Relationships Codes Notebook Steps Feedback WPs & Docs Expenses Summary

Activity: M18000 0-10 Contract 99C0016 Project: 108791

Activity Code	Code Value	Description
Construction Contract Delay	D0	No Current Problems (All Phases)
Construction Contract Status	U	Construction Underway - On or Ahead of Schedule
Contract	Prim	Primary
Task Organization	213	B2M1396-CONST DIV4/NOAD-SELA/ORL PAR
Contracting Type	A	Competitively Bid, Fixed Price, Normal Procedure
Asset Class	C	Construction Expense (E&P)
WCC (CEPMS) - Civil Works	13000	Pumping Plants
Permanent Feature (R)	J	Channels And Canals

Assign Remove

Portfolio: All Projects User: aledvpm Data Date: 02-Aug-04 Access Mode: Shared Baseline: Current Project

Status and Delay Codes



US Army Corps
of Engineers

Resident Management System

File Help

RMS **Flagstaff Project Office**

Select Contract Local Office District Office District Library System Library Summary Reports Exit RMS

Local Office - Office Description

[Office Description](#)
[Office Personnel](#)
[Office Policy](#)
[Office Documents](#)
[Office User Entries](#)
[P2 Projects](#)
[Local Milestones](#)
[Mod Routing Slip](#)
[Interface Schedules](#)
[User Permissions \(2.37\)](#)

Add Edit

Construction Div
Hurricane Prote
Task Force Gu
Contracting Div
Operations Div
PP&PM Div
Arizona/Nevada
Las Vegas f
Roadrunner
Flagstaff
Luke Pr
Tres Ric
Yuma P
Tucson Res
District Manage
Environmental C
High Desert Are
SoCal Area Offi
GRC -District M
Gulf Region Nor
Gulf Region Sou

Flagstaff Project Office

Edit Office Information

Close

Parent Office Roadrunner Resident Office

Office Symbol CESPL-CD-AF Office Type PROJECT OFFICE

Office Name Flagstaff Project Office Office Manager Rodriguez, Joel

Position Title

Address PO Box M
Flagstaff, Arizona 86002

Phone No. 928-779-0578 Kayenta 928-69
Fax No. 928-779-5324

(example -117.171261) (example 34.500465)

Location Office Longitude -111.6499 Office Latitude 35.1988

P2 Org Code L1M0B50 Prefix Code for Change Requests AF

Time Zone (GMT-07:00) Mountain Time (US & Canada) ☐ Observe daylight savings time

Office POCs

CCASS Focal Point Email Notification to CCASS Focal Point when DD2626 exported to CCASS

ACASS Focal Point Email Construction AE evaluation information to ACCASS Focal Point

PD² Coordinator Email Mod Information to PD² Coordinator when Mod Completed

You can download the P2 Task Organizations by using the lookup



US Army Corps
of Engineers

Download P2 Data

Resident Management System
File Help

RMS **Flagstaff Project Office**

Select Contract Local Office District Office District Library System Library Summary Reports Exit RMS

Local Office - P2 Projects

[Office Description](#)
[Office Personnel](#)
[Office Policy](#)
[Office Documents](#)
[Office User Files](#)
[P2 Projects](#)
[Local Milestones](#)
[Mod Routing Slip](#)
[Interface Schedules](#)
[User Permissions \(2,37\)](#)

Import P2 Projects Export P2 Projects Unlinked P2 WBS's Unlinked Contracts Linked Contracts

Import from P2

Future Contracts

- Task Amount
- Design By
- Contract Type
- Project Scope of Work
- Contract Status
- Primary Delay Code
- Project - Customer Issues
- Project - USACE Issues
- System Milestone Events

Awarded Contracts

- Project Scope of Work
- Project - Customer Issues
- Project - USACE Issues
- Fiscal Completion

Import Projects from P2 for

☒ Flagstaff Project Office
☐ Flagstaff Project Office including sub-offices
☐ All offices

Import P2 Projects

Last Import for Flagstaff Project Office -- 06/25/09 04:25 pm

Once you have entered the P2 Task Organization Code for a particular office, you are ready to download the available P2 projects for that office. Click on the Home button, select the office you want to download P2 projects for, and then click the Summary button. The program will display the option P2 Projects and you should select that option.



US Army Corps
of Engineers ®

Unlinked P2 WBS's

Resident Management System

File Help

RMS Gulf Region Northern District

Select Contract Local Office Division Office District Library System Library Summary Reports Exit RMS

Local Office - P2 Projects

[Office Description](#)
[Office Personnel](#)
[Office Policy](#)
[Office Documents](#)
[Office User Entries](#)

[P2 Projects](#)

[Local Milestones](#)
[Mod Routing Slip](#)
[Interface Schedules](#)

Import P2 Projects Export P2 Projects **Unlinked P2 WBS's** Unlinked Contracts Linked Contracts

WBS's for Gulf Region Northern District ☐ Show Invalid WBS's

Project ID	Project Title	WBS No.
142450	CAP 067295 CJSOAC Ops Ctr	60000.61000

WBS Title **W916QW-05-D-00050010 - PN 67295** ☐ Invalid WBS

P2 Tasks

Task Code	Task Name	Amount
C0124	Mod 0004, HVAC and Raised Floor	\$100,000.00

Project Scope of Work

Link this Project to : Existing RMS Contract New RMS Contract

1 P2 Projects/WBS's not linked to a Contract for Gulf Region Northern District



US Army Corps
of Engineers

Identify and Link P2 Projects to RMS Contracts

Resident Management System

File Help

RMS Flagstaff Project Office

Select Contract Local Office District Office District Library System Library Summary Reports Exit RMS

Local Office - P2 Projects

Office Description
Office Personnel
Office Policy
Office Documents
Office User Entries
P2 Projects
Local Milestones
Mod Routing Slip
Interface Schedules
User Permissions (2.37)

Import P2 Projects Export P2 Projects Unlinked P2 wBS's Unlinked Contracts Linked Contracts

Contracts Not Linked to a P2 Project for Flagstaff Project Office

Contract ID/No	Contract Title
DACW09-01-C-0009 NA	Clifton Recreation Development
L1002657	

Contract ID/Number DACW09-01-C-0009 NA

Contract Scope of Work

Final Pay Estimate sent to District

Recreational Vehicle Park with shade structures, comfort station, 55 camping units: 32 single, 23 double access to a comfort station with showers, lighting, and paths. Baseball field and picnic ramadas.

Link this Contract to : P2 Project

2 of 8 Contracts not linked to a P2 Project for Flagstaff Project Office

Select P2 Project

Search Characters

Search By Project ID

☐ Flagstaff Project Office
☐ Flagstaff Project Office including sub-offices
☒ All offices

P2 Projects

Project ID	Project Title	wBS No.	wBS Title
104104	J09CA0067020-Camp Elliot - MT	80000.0 60000.20	Construction Contract
104311	J09CA048601 CON/HTRW/Minter	60000.1	Construction - Minter Airport Soil Sampling
104391	J09CA203103 HTRW/Camp San Luis	80000.0 1.61000	Construction - Contract A
104590	CAMPO BORDER PATROL STATION	M.60000.61000	Construction - Contract A
104700	Sweetwater Ecosys Rest,CA(206)	30000.300S0	CAP Construction - Contract A
104743	San Luis Rey River, CA	30000.300S091	SLR, Phase 2
104743	San Luis Rey River, CA	30000.300S0911	SLR, Phase 3 & 3 R1
104743	San Luis Rey River, CA	30000.300S09111	SLR, Phase 3 R2
104759	Tucson Drainage Area, AZ	30000.300S1	Phase II B Construction - Basins 1, 2, 3 & Channel Improv
104770	Rio Salado Phoenix & Tempe, AZ	30000.30001.300091.300S1	Construction Contract - Tempe Phase IV - Northbank
104772	Norco Bluffs, CA	30000.300S0	DACA09-02-D-00140001 - Norco Bluffs Z2 Hydr

P2 Tasks

Task Code	Task Name	Amount
A1865	Contract- MT Surface Clearance	\$1,400,000.00

Project Scope of Work / Project Issues - USACE

Record 1 of 648.

OK Cancel

Another area where
you can link a P2
Project to an RMS
contract is on the
Contract
Administration screen.



Controlling the RMS - P2 Interface

US Army Corps
of Engineers ®

Contract ID - L1001373 Contract No. - W912PP-07-C-0010

File Help

RMS RMS Training Contract

Close Contract Administration Finances QA/QC Submittals Schedules Closeout Import/Export Contract Reports

Administration - Contract Setup

Administration/Funding Payment/Modifications Quality Assurance Submittals/Schedule

[Contract Status](#)
[Contract Description](#)
[Contract Personnel](#)
[Contract Documents](#)
[Contract Setup](#)
[P2 Projects](#)
[Correspondence](#)
[Request for Information](#)
[Contract User Entries](#)
[Prime Contractor](#)
[Subcontractors](#)
[Contractor Insurance](#)
[Contractor Payrolls](#)
[Labor Interviews](#)

Administration CEFMS Database Service

☒ Will CEFMS be used for downloading Finances and uploading Payments ?

☒ Will this contract be linked to P2 ? ☒ Use P2 data prior to award ? ☒ Use only one Phase ?

☒ Do you want to use QAS with this contract?

☒ Do you want to use QCS with this contract?

☒ Do you want to answer RFI's with two-way RFI Form ?

☒ Do you want to track Contractor's Insurance in RMS ?

☒ Do you want to track Contractor's Payrolls in RMS ?

☒ Do you want to track Labor Interviews in RMS ?

☒ Will this contract require a DD1354 Transfer Document ?

Contractor Correspondence Entered By

Insurance Entered By

Payroll Entered By

RFI Entered By

Category Codes for

Funding

☒ Track Funding at Funding Account Level, pre-plan Obligations for payment on all CLINS

☐ Track Funding at Project Level, compute Obligation amounts for payment based on available funds

☐ Track Funding at Project Level, manually enter Obligation amounts for payment

Currency Type

Payment

☒ Progress Payments - Allow Additional Earnings not included in Activity Earnings



US Army Corps
of Engineers ®

Multi-Phase Contracts in RMS

Contract ID - B2000650 Contract No. - W912P8-08-C-0038

File Help

RMS HPO IHNC-02, IHNC Hurricane Protection

Close Contract Administration Finances QA/QC Submittals Schedules Closeout Import/Export Contract Reports

Schedules - Milestone Schedule

[Activity Schedule](#)
[Milestone Schedule](#)
[Placement Schedule](#)
[Feature Schedule](#)

Active Phase Phase 01 - Main Gates

Award Duration 1,152 days Current Duration 1,152 days

Add Edit Delete Find ☐ Show System Events Only All Events

	Milestone Event	Original Date	Scheduled Date	Scheduled Time	Actual Date	Status
▶	◆ Contract Award				04/03/2008	Completed
	◆ NTP Acknowledged				04/05/2008	Completed
	◆ Construction Start Date		09/01/2008		11/03/2008	Completed
	◆ Advance Measures in Place		08/20/2009			Reschedule
	◆ Contract Required Completion	06/01/2011	06/01/2011			Scheduled
	◆ Beneficial Occupancy Date	06/01/2011	06/01/2011			Scheduled
	◆ 100 yr Level of Prot in Place		06/01/2011			Scheduled
	◆ Contract Physical Completion		12/01/2011			Scheduled
	◆ Contractor Evaluation Date		12/01/2011			Scheduled
	◆ Construction Completion		12/01/2011			Scheduled
	◆ Contractor Final Payment		02/15/2012			Scheduled
	■ Release of Claims Date		02/15/2012			Scheduled
	◆ AE Evaluation Date		N/A		N/A	N/A
	◆ Transfer Document Date		N/A		N/A	N/A
	■ Interim Evaluation - AO					Not Scheduled
	■ Next Interim Evaluation - AO					Not Scheduled
	■ Final Evaluation - AO					Not Scheduled
	◆ Red Zone Meeting					Not Scheduled
	◆ Project Fiscal Completion					Not Scheduled

◆ System Milestones ■ District Milestones ● Contract Milestones

Milestone Event 1 of 20 for [Main Gates]



US Army Corps
of Engineers ®

Information Interchanged from RMS to P2

Contract ID - L1001373 Contract No. - W912PP-07-C-0010

File Help

RMS

RMS Training Contract

Close Contract

Administration

Finances

QA/QC

Submittals

Schedules

Closeout

Import/Export

Contract Reports

Import/Export - Import P2

[Import/Export QCS](#)
[Import/Export QAS](#)
[Import P2](#)
[Import Submittals](#)
[Import Real Property](#)
[Import Another Contract](#)
[Export Mods List](#)

Import from P2

Awarded Contract

- Project Scope of Work
- Project – Customer Issues
- Project – USACE Issues
- Fiscal Completion

☒ Import Projects for current contract

☐ Import Specific P2 Project

Import from P2

Last download - 06/25/09 03:07 pm



US Army Corps
of Engineers ®

P2 - RMS Interface

- RMS defined dates are maintained via constraints in Primavera
- Manually entered overrides will be overwritten from RMS during the next update cycle
- Interface does NOT reschedule the project



US Army Corps
of Engineers ®

P2 - RMS Interface

- You **MUST** use construction plug-ins
- To remove constraints
 - Remove the constraint
 - Reschedule the project
 - Remove the date from RMS
 - Reschedule project

Activities

Layout: Jim's Classic WBS Layout Filter: All Activities

Activity ID	Activity Name	Start	Finish	RMS Current Contract	RMS Interface	Schedule % Complete
Project: 126994 CAP 063628 STE PREP AND UTIL W		28-Mar-05	28-Mar-05	0.00		0%
WBS: 126994.01000	Project Management Plan (PMP)	28-Mar-05	28-Mar-05	0.00		0%
WBS: 126994.40000	Design	28-Mar-05	28-Mar-05	0.00		0%
WBS: 126994.42000	Value Engineering/Value Management	28-Mar-05	28-Mar-05	0.00		0%
WBS: 126994.60000	Construction	28-Mar-05	28-Mar-05	0.00		0%
A0370	Project Closeout		28-Mar-05			0%
WBS: 126994.60000.61000	Construction - Contract A	28-Mar-05	28-Mar-05	0.00		0%
C0110	Construction NTP Acknowledged	28-Mar-05			RMS_M_NTP_ACKNOWLEDG	0%
C0120	Contract	28-Mar-05	28-Mar-05		RMS_A_CONTRACT	0%
C0200	Beneficial Occupancy Date		28-Mar-05		RMS_M_BEN_OCC_DATE	0%
C0190	Physical Completion		28-Mar-05		RMS_M_CONS_COMP_PHYS	0%
C0230	Fiscal Completion		28-Mar-05		RMS_M_CONS_COMP_FISC	0%
C0100	Contract Award		28-Mar-05		RMS_M_CONTRACT_AWARD	0%
C0170	Construction Completion		28-Mar-05		RMS_M_CONS_COMPLETE	0%
C0240	Transfer Document Date		28-Mar-05		RMS_M_TRANSFER_DOC	0%
C0180	Contract Required Completion		28-Mar-05		RMS_M_REQ_COMPLETE	0%
C0210	AE Evaluation Date		28-Mar-05		RMS_M_AE_EVALUATION	0%
C0220	Contractor Evaluation Date		28-Mar-05		RMS_M_CONTR_EVAL	0%
C0130	Supervision & Administration	28-Mar-05	28-Mar-05		RMS_L_SNA	0%
C0140	Management Reserve	28-Mar-05	28-Mar-05		RMS_L_MGMT_RESERVE	0%
C0150	Other Direct Costs	28-Mar-05	28-Mar-05		RMS_L_OTH_DIR_COSTS	0%
C0160	Direct Design Costs	28-Mar-05	28-Mar-05		RMS_L_DIR_DESN_COSTS	0%
WBS: 126994.80000	Operation & Maintenance			0.00		0%
WBS: 126994.90000	Real Estate			0.00		0%

Add
 Delete
 Cut
 Copy
 Paste
 Resources
 Rsrc by Role
 Roles
 Activity Codes
 Predecessors
 Successors

Activities



Layout: Jim's Classic WBS Layout

Filter: All Activities

Activity ID	Activity Name	Start	Finish	RMS Current Contract	RMS Interface	Schedule % Complete
WBS: 100008.3000.30D50	Construction - Contract A	30-Mar-05	30-Mar-05	0.00		0%
CON505	Contract Nego/Awd Docs	30-Mar-05	30-Mar-05			0%
CON500	Contract RTA		30-Mar-05			0%
CON495	Receive Sponsor Construction Funds		30-Mar-05			0%
CON510	CBD Announcement	30-Mar-05	30-Mar-05			0%
CON520	Contract Adv/RFP Issued		30-Mar-05			0%
CON530	Davis Bacon Wage Rates	30-Mar-05	30-Mar-05			0%
CON540	Gov't Estimate (IGE)	30-Mar-05	30-Mar-05			0%
CON550	Open Bids		30-Mar-05			0%
CON560	Abs of Bids/Rec of Nego	30-Mar-05	30-Mar-05			0%
CON570	Cert Low Bid/Prep Contract Docs	30-Mar-05	30-Mar-05			0%
CON600	Rec Bonds/Prep NTP	30-Mar-05	30-Mar-05			0%
CON675	Evaluate A/E Contractor	30-Mar-05	30-Mar-05			0%
CON685	Eval Constr Contractor	30-Mar-05	30-Mar-05			0%
CON580	All Other Awd Docs	30-Mar-05	30-Mar-05			0%
CON490	Budgeted Construction Contingency	30-Mar-05	30-Mar-05			0%
CON620	Construction NTP Acknowledged	30-Mar-05			RMS_M_NTP_ACKNOWLEDG	0%
CON630	Contract	30-Mar-05	30-Mar-05		RMS_A_CONTRACT	0%
CON660	Physical Completion		30-Mar-05		RMS_M_CONS_COMP_PHYS	0%
CON700	Contract Fiscal Completion		30-Mar-05		RMS_M_CONS_COMP_FISC	0%
CON590	Contract Award		30-Mar-05		RMS_M_CONTRACT_AWARD	0%
CON640	Construction Completion		30-Mar-05		RMS_M_CONS_COMPLETE	0%
CON710	Contract Transfer Document Date		30-Mar-05		RMS_M_TRANSFER_DOC	0%
CON650	Contract Required Completion		30-Mar-05		RMS_M_REQ_COMPLETE	0%
CON680	AE Evaluation Date		30-Mar-05		RMS_M_AE_EVALUATION	0%
CON690	Contractor Evaluation Date		30-Mar-05		RMS_M_CONTR_EVAL	0%
CON610	Issue NTP		30-Mar-05			0%
WBS: 100008.30D00.30DV0	E&D During Construction	30-Mar-05	30-Mar-05	0.00		0%
WBS: 100008.30D00.30F00	Project Closeout	30-Mar-05	30-Mar-05	0.00		0%
WBS: 100008.00500	Project Management Plan (PMP)	10-Feb-04 A	29-Sep-04 A	0.00		100%
WBS: 100008.21000	Recon/Sec 905(b) Studies	10-Feb-04 A	29-Sep-04 A	0.00		100%

Add
 Delete
 Cut
 Copy
 Paste
 Resources
 Rsrc by Role
 Roles
 Activity Codes
 Predecessors
 Successors

Activities



Layout: Jim's Classic WBS Layout

Filter: All Activities

Activity ID	Activity Name	Start	Finish	RMS Current Contract	RMS Interface	Schedule % Complete
Project: 100008 Elm Creek, Abilene		10-Feb-04 A	16-Jan-14	0.00		11.04%
WBS: 100008.10000 CERCLA Remedial Action - Construction		30-Mar-05	30-Mar-05	0.00		0%
WBS: 100008.10000.10100 Construction		30-Mar-05	30-Mar-05	0.00		0%
RAC1000	Start RA-C	30-Mar-05				0%
RAC1030	Perform RA-C Activities	30-Mar-05	30-Mar-05			0%
RAC1040	Prepare Plans (SAP, HASP, Waste Disposal, ...)	30-Mar-05	30-Mar-05			0%
RAC1050	Develop Construction & Start-up (C&S) Manual	30-Mar-05	30-Mar-05			0%
RAC1060	Perform C&S Support	30-Mar-05	30-Mar-05			0%
RAC1070	Conduct Initial Operator Training	30-Mar-05	30-Mar-05			0%
RAC1080	Conduct Commissioning & Start-up	30-Mar-05	30-Mar-05			0%
RAC1090	Develop Operating Manuals	30-Mar-05	30-Mar-05			0%
RAC1100	Conduct Final Operator Training	30-Mar-05	30-Mar-05			0%
RAC1110	Prepare RA-C Completion Report	30-Mar-05	30-Mar-05			0%
RAC1120	Write Draft Report	30-Mar-05	30-Mar-05			0%
RAC1130	Review Draft Report	30-Mar-05	30-Mar-05			0%
RAC1140	Incorporate Comments into Draft Report	30-Mar-05	30-Mar-05			0%
RAC1150	Prepare Final RA-C Report	30-Mar-05	30-Mar-05			0%
RAC1160	Finish RA-C		30-Mar-05			0%
RAC1010	Contract Award		30-Mar-05		RMS_M_CONTRACT_AWARD	0%
RAC1020	Contract	30-Mar-05	30-Mar-05		RMS_A_CONTRACT	0%
WBS: 100008.10000.10200 Supervision & Administration (S&A)		30-Mar-05	30-Mar-05	0.00		0%
RAC1170	Perform S&A Activities	30-Mar-05	30-Mar-05			0%
RAC1180	Pre-Construction Conferences	30-Mar-05	30-Mar-05			0%
RAC1190	Administer Contract (Process Pay Estimates, ...)	30-Mar-05	30-Mar-05			0%
RAC1200	Conduct Technical Supervision	30-Mar-05	30-Mar-05			0%
RAC1210	Perform Field Testing	30-Mar-05	30-Mar-05			0%
RAC1220	Monitor Compliance with Work Plans	30-Mar-05	30-Mar-05			0%
RAC1230	Conduct Final Inspection		30-Mar-05			0%
WBS: 100008.00500 Project Management Plan (PMP)		10-Feb-04 A	29-Sep-04 A	0.00		100%
WBS: 100008.21000 Recon/Sec 905(b) Studies		10-Feb-04 A	29-Sep-04 A	0.00		100%
WBS: 100008.22000 Feasibility Studies		01-Oct-04 A	16-Jan-14	0.00		3.27%

Add
 Delete
 Cut
 Copy
 Paste
 Resources
 Rsrc by Role
 Roles
 Activity Codes
 Predecessors
 Successors



...





US Army Corps
of Engineers ®

P2 - RMS Interface

Questions?
